



**THE CONSTRUCTION OF  
ATHINA  
PORTIONS 66 OF FARM 443, BRAKKLOOF**

**ENVIRONMENTAL MONITORING CHECKLIST  
AND REPORT:  
PRE-CONSTRUCTION AND CONSTRUCTION PHASE**

**September 2024**

Complied by:  
**Lizelle Genade**  
(EAP 2023/7793)  
[lizelle@ecoroute.co.za](mailto:lizelle@ecoroute.co.za)

<b>Environmental Authorisation Holder</b>	Athina development (PTY) Ltd
<b>Environmental Control Officer</b>	Bluepebble CC
<b>EA Reference Number</b>	DEA&DP REF: 16/3/3/1/D1/14/0028/22
<b>OSCAE File Reference</b>	18/66&67/443/PB
<b>CARA Reference Number</b>	13/10/6/3K451
<b>WULA Licence Number</b>	02/K60G/CI/13424

<b>Attention:</b>	
Department of Environmental Affairs and Development Planning	<a href="mailto:DEADPEIAAdmin.George@westerncape.gov.za">DEADPEIAAdmin.George@westerncape.gov.za</a>
	<a href="mailto:Zaahir.Toefy@westerncape.gov.za">Zaahir.Toefy@westerncape.gov.za</a>
	<a href="mailto:Dorien.Werth@westerncape.gov.za">Dorien.Werth@westerncape.gov.za</a>
Bitou Municipality	<a href="mailto:aminne@plett.gov.za">aminne@plett.gov.za</a>
The Department of Water and Sanitation.	<a href="mailto:asam@bgcma.co.za">asam@bgcma.co.za</a>

## 1. Compliance Ratings, Non-Compliances and Detections

Compliance with the EA/EMPr is rated according to the system detailed below:

COMPLIANCE RATING	DEFINITION	PERCENTAGE
Full Compliance	Depicts EA/EMP conditions where the contractor is fully compliant with the particular condition. Where compliance with the condition is completed and compliant, the condition will be removed from the reporting.	100%
Partial Compliance	Depicts EA/EMP conditions where the contractor is partially compliance or where additional actions are required to ensure compliance.	60% -99%
Non-Compliance	Depicts EA/EMP conditions where the contractor is non-compliant.	< 60%
Not commenced yet	Depicts EA/EMP conditions that cannot be monitored or conditions associated with aspects of the project that have not yet commenced.	

Non-compliance with a condition of this environmental authorisation or EMPr is an offence in terms of Section 49A(1)(c) of the National Environmental Management Act, 1998 (Act no. 107 of 1998, as amended).

Document of reference	Activity in terms of authorization	Observation & Corrective action to be taken where necessary	Pic no.	Responsibility
-----------------------	------------------------------------	---	---------	----------------

EMPr p53	<b>Authorization - Authorisations, Licences and Permits (1)</b>			
	All necessary authorisations, permits and licences must be obtained by the Applicant prior to construction commencement. This includes permits for the removal of protected plants.	Yes, NFA licenses will be applied for when and if necessary		EA Holder

EMPr 53	<b>Method statements (1)</b>			
	Has Method Statements been submitted by the Applicant/ Contractor to the ECO and DEA&DP for approval. Method Statements must be adhered to by the Applicant/ Contractor. <ul style="list-style-type: none"> <li>❖ Stormwater management</li> <li>❖ Erosion control</li> <li>❖ Shoring (if required)</li> <li>❖ Dust control</li> <li>❖ Stockpile and storage areas</li> <li>❖ Site preparation and construction</li> <li>❖ Installation of services and roadways</li> <li>❖ Road upgrade</li> <li>❖ Solid waste management</li> <li>❖ Storage of hazardous materials (if applicable)</li> <li>❖ Standard emergency procedures</li> </ul>	Method Statement have been received by Civil Engineer. Thank you. All placed in environmental file, kept on site.		Contractor/PM

EMPr 54, 55	<b>Education of Site Staff on General and Environmental Conduct - A general regard for the social and ecological wellbeing of the site and adjacent areas is expected of the site staff. (7)</b>			
	Has all contractors, sub-contractor and delivery personnel been briefed on the Construction Phase Management Rules (Appended to the EMPr)? The main contractor must do these briefings before his staff will be allowed to work on the Estate. The main contractor remains the liable person.	Yes. Ongoing. Copy of environmental training has been given to contractor. Suggested they stick it onto		Contractor/PM

		container wall for all to have access to dos and don'ts and to ensure they comply with EMPr. Should more induction be required as new contractors start on site, project manager need to inform ECO.		
	Has all construction staff been adequately educated by the ECO as to the provisions included in the EMPr, and in terms of general environmentally friendly practice and was language considered during training?	Yes, Two inductions have already been done. One before demolition and one before construction of access road. Ongoing. More inductions will be done as needed. Contractor to communicate this with ECO.		Contractor/ ECO
	Has all contractors, sub-contractors and casual labourers acknowledged their understanding of the EMPr and environmental responsibilities by signing an induction attendance record?	Yes, Attendance register attached to Hard copy of training left on site. Any new staff needs to sign as well when inducted.		Contractor/ ECO
	Has all staff, operating equipment, shall be adequately trained and sensitised to any potential hazards associated with their tasks?	Yes		Contractor
	Has staff been made aware that they are not to make excessive noise e.g. shouting, hooting.	Yes		Contractor/ ECO
	Where staff turnover is high and with additional appointment of Sub-contractors, it may be necessary to undertake additional induction training sessions. Contractor is responsible for all staff to be inducted and made aware of EA and EMPr. Hard copy of induction left on site for use by Contractor.	Yes, Contractor's responsibility, but ECO is available to do more inductions if required.		Contractor
	Does the Contractor keep records of all environmental training sessions, including names, dates and the information presented?	Yes, on file on site.		Contractor

<b>EMPr 55</b>	<b>Site establishment (11)</b>			
	Has development area, area of works and spoiling areas been clearly identified and demarcate using correct demarcation methods?	Netting has been erected to demarcate all no-go areas. Fencing has also commenced which will keep all staff out of 6m protected servitude area. Map of laydown area approved by ECO.	5,12, 25,26, 27,32, 34,35, 7,	Contractor
	Has material stockpile sites been established within site camp s approved by ECO?	Yes, stockpiles of building material is close to areas of work being done.		Contractor
	Has a waste disposal area been established within site camp as approved by ECO?	A caged bin lined with bidum has been placed on site for waste management.	19,57	Contractor

	Has necessary ablutions facilities, on-site sanitation been established within site camp as approved by ECO?	Yes, toilet on site. Secured against winds and serviced regularly.	13,20	Contractor
	Is temporary toilets serviced and cleaned on a regular basis.	Yes, weekly		Contractor
	Has a rest area for smoking and eating been established for workers?	Yes, around container area.		Contractor
	Has water been provided for staff for drinking and washing?	Yes	38	Contractor
	Are all staff only using facilities provided for them, as opposed to ad-hoc alternatives (e.g. fires for cooking, the use of surrounding bush as a toilet facility is strictly forbidden).	Yes, monitored by foreman.		Contractor
	Any signs of open fires being made on site?	None observed on site visit		Contractor
Fire Management	Are there firefighting equipment on site?	None observed. Apologies if I missed it. Some machinery have fire extinguishers on them as standard practice.		Contractor
	Is smoking only done in designated areas where it does not pose a fire risk or adding to pollution?	Yes, no smoking or cigarette butts observed. Have requested a tin to be placed close to container to prevent any butts being discarded on site.		Contractor

	<b>Access (4)</b>			
	Are all vehicles staying clear of adjacent properties and any other no-go areas?	Yes	16	Contractor
	Was any trespassing on private / commercial properties adjoining the site observed or reported?	None reported or observed.		Contractor
	Does drivers of heavy-duty vehicles exercise care when travelling to and from the site – and adhere to all legally enforceable requirements?	Yes		Contractor
	Are all machinery in good working order?	Yes, no leaks observed	6,8,9,28 29,36, 42,49	

	<b>Site Management (5)</b>			
	Is construction footprint limited to the construction area? And has it been marked to the satisfaction of ECO?	Yes. Servitude area has and no-go area have been demarcated and is currently being fenced.		Contractor
	Are all activities, materials, equipment, and personnel restricted to construction footprint, and not within the no-go area specified?	Yes		Contractor
	The applicant will be held responsible for any clean-up in the dune environment resulting from failure by the contractors or suppliers to properly secure material.	Yes, will be done if this occurs. No issues observed on site visits.		Contractor
	Has adequate drainage and erosion protection been provided around the site and where necessary?	Drainage and erosion not an issue at the moment. Service are being installed and the dune		Contractor

		sand allows for easy drainage, runoff and erosion not expected during this phase. Closely monitored by contractor. Stormwater channel next to access road being installed.	50	
	Is dust pollution managed on all access points and other cleared surfaces? Must be dampened whenever necessary and especially in dry and windy conditions to avoid excessive dust. Alternatively, a binding product such as Dustex (supplied by Patch Industrial Supplies) could be used.	No dust pollution observed on site visits.		Contractor

<b>EMPr 58</b>	<b>Waste management (9)</b>			
	Is an integrated waste management system in place, which includes waste minimisation, waste recycling and the proper storage and disposal of waste, which does not impact of the health of the environment and human health?	Lined caged bin have been placed on site	19,57	Contractor
	Is waste being sorted according to the waste hierarchy, discarded in the appropriate manner and recorded (slips from facilities required)?	Yes, waste is sorted and removed on a regular basis.		Contractor
	Is site free of litter?	No	14,15, 22	Contractor
	Has an adequate number of appropriate bins been provided for construction workers and staff at locations around site and where they consume food, to collect all domestic refuse, and to minimise littering?	Yes. Discussed above.		Contractor
	Is ongoing awareness of the need to avoid littering being conducted with staff?	Yes, but needs to be enforced by foreman on site daily.		Contractor
	Any evidence of waste being buried or burned?	None observed on site visits		Contractor
	Any evidence of excavation and use of rubbish pits?	None observed on site visits		Contractor
	Is waste removed from the site on a weekly basis?	Yes		Contractor
	Is building rubble removed from site on a regular basis?	Rubble on site removed.	7,53	Contractor

<b>EMPr 56</b>	<b>Storage and stockpiling (11)</b>			
	The contractor will be allowed to erect green storage sheds/huts within the boundaries of the building site and to a maximum height of 2,4 m. The position of such structures must be indicated on the site diagram, which must be approved by Estate Management & ECO.	Yes		Contractor
	Choice of location for equipment lay-down and storage areas must take into account prevailing winds, distances to "No Go" areas, general on-site topography and water	Yes. Will be ongoing and change as new phases are implemented.		Contractor

	erosion potential of the soil. Impervious surfaces, bunded areas or drip trays must be provided where necessary.			
	Material stockpiles must be protected against rain and flooding.	Yes.		Contractor
	Equipment lay-down and storage areas must be designated, demarcated and signed.	Yes.		Contractor
	Stockpiles must not exceed 1.5m in height, must be covered with shade cloth or similar, to prevent erosion and any invasive alien species that begin to grow within it must be removed.	Yes. Will be monitored by Foreman and ECO.		Contractor
Hazardous Materials	Material Safety Data Sheets (MSDSs) shall be readily available on site for all chemicals and hazardous substances to be used on site. Where possible and available, MSDSs must additionally include information on ecological impacts and measures to minimize negative environmental impacts during accidental releases or escapes.	Awaiting from Foreman. To be kept on site within container.		Contractor
	Cement and other potential environmental pollutants must be stored within an impermeable bunded, roofed and sign posted area.	Yes. Stored in container.		Contractor
	The mixing of cement must be done on Rhino board.	Cement mixed in concrete trays.	33,37, 52	Contractor
	Minimise fuels and chemicals stored onsite.	Yes		Contractor
	Install bunds and take other precautions to reduce the risk of spills.	To be done		Contractor
	Implement a contingency plan to handle spills, so that environmental damage is avoided. Method statement required.	Yes. Received.		Contractor

<b>EMPr 57</b>	<b>Erosion and Stormwater Control (5)</b>			
	Soil disturbance during the removal of alien invasive plants must be minimised as much as possible.	Yes		Contractor
	Storm water control must be undertaken to prevent soil loss and erosion impacts from the site.	Foreman to monitor daily.		Contractor
	Erosion prevention and control measures must be implemented. This may be by the use of mulch bags or silt fences. The engineer must provide a method statement for site specific erosion methods.	This will be implemented on completion of service installation and access road construction.		Contractor
	Provision shall be made for storm water management measures that will ensure effective run-off control and prevent erosion at run-off points.	This will be implemented on completion of service installation and access road construction.		Contractor
	The site must be stabilised where necessary using available materials, where possible. It is recommended that exposed soils are covered with wood chips, and tree branches used to create berms. Any cut alien vegetation on site can be utilised for this purpose if it is without seed.	Yes		Contractor

<b>EMPr 57</b>	<b>Topsoil to be used in rehabilitation (3)</b>			
	Is topsoil stored separate from other materials?	Topsoil stored close to excavated area. To be used again for infill.	3	Contractor
	Topsoil piles no higher than 1.5m	Topsoil stored close to excavated area. To be used again for infill.		Contractor
	Topsoil covered until used in rehabilitation or agricultural practise.	Topsoil stored close to excavated area. To be used again for infill.		Contractor

<b>EMPr 58</b>	<b>Installation of services and roadways (6)</b>			
	Topsoil for trenching along the route for installation of services to be removed to 150 mm deep, maintained and replaced as the final compacted layer in the road reserves.	Yes, will be monitored by foreman		Contractor
	In trenches of slopes over 25% grade - bio textiles and reseeding to be used to rehabilitate and protect the compacted topsoil.	Yes, will be monitored by foreman		Contractor
	Install a series of berms across the internal access road to retard flow from higher areas.	To be done in next phase.		Contractor
	Building sites need to be surrounded with a trench and berm arrangement to contain all building site runoff.	To be done in next phase.		Contractor
	The proposed gabion retention pond needs to be constructed first with site runoff discharged into it.	To be done in next phase.		Contractor
	The gabion retention/silt pond needs to be cleaned out prior to handing over the internal services.	To be done in next phase.		Contractor

<b>EMPr 8</b>	<b>Conservation of the Natural Environment (17)</b>			
Fauna and Flora	Areas which are identified by the Environmental Control Officer (ECO) as being ecologically sensitive on or adjacent to the site are to be suitably demarcated to prevent damage by construction practices. These areas are to be recognised as "no-go" areas.	Netting erected to demarcate no-go areas		Contractor
	No natural vegetation may be cleared without prior permission from the ECO and if applicable from any relevant authority. Indigenous vegetation that is removed is to be replanted either back to the point from which it was taken or must be replaced by new relevant indigenous vegetation.	Yes, botanist have been appointed for this purpose. Plants kept in nursery.	23	Contractor
	All alien invasive plant species must be continuously removed around the site. The best way to do this is to remove the plants from the roots by hand and leave the plants in the sun to dry out and die before disposal. Please refer to the Alien Plant Control Programme.	Yes, done. Dead plant to be removed.	2, 24	Contractor



	Disturbance to birds, animals and reptiles and their habitats must be minimized wherever possible.	Yes, care is taken not to disturb fauna on site.		Contractor
	Permission must be attained from the relevant authority (DFFE) to remove any of the specially protected Milkwood trees ( <i>Sideroxynoninerme</i> ) that still occur on the properties, even though they are small due to the recent fire.	Yes, NFA license will be applied for when removal of protected tree species are required. Currently trees are marked to ensure no damage. Or disturbance.	11,31	Contractor
	The proposed development will not have any flammable natural vegetation remaining. The fire risk was mostly posed by alien vegetation, which will be removed by the development.	Yes, alien vegetation removal in progress and management thereof will be ongoing. Alien vegetation removed being chipped and used in pathway to beach.		Contractor
	Clearing of vegetation for the construction phase must be undertaken in a phased approach such that clearing for the roads and services are undertaken first, and clearing for construction of dwellings is undertaken on approval of building plans and OSCAE permit. Details to be provided in method statement that must be compiled by the appointed Contractor for each phase of the development.	Yes. Ongoing. Monitored by ECO		Contractor
Preservation of natural habitats	Prior to the commencement of clearing the proposed building site, the contractor must undertake vegetation search-and-rescue on the site. This operation is a legal requirement to ensure that any endangered vegetation species is transplanted prior to work commencing on the erf.	Yes, has been conducted by botanist already appointed. Ongoing.		Contractor
	A Landscape consultant must be appointed prepare a landscape plan for implementation in the private and common areas.	Landscape plan has been done in the common areas and along access road. Will be implemented once construction is complete.		Contractor
Landscape Connectivity	A six (6) metre wide ecological corridor along the northern boundary of the development must be establish and maintain. The 6m wide servitude serves as a minor corridor for smaller wildlife, linking the wetland to the west with the coastal dunes to the east. The servitude must not be disturbed during construction activities and be cleared of invasive alien plants.	No-go area demarcated		Contractor
	No structures or infrastructure may be constructed in this servitude without authorisation. This ecological servitude must not be fenced on the eastern and western boundaries. The erection of perimeter fencing must exclude the eastern and western boundary of the corridor to allow for free movement of wildlife through the corridor	Yes, being adhered to. Ongoing. Monitored by ECO		Contractor
	Services (i.e., sewer line, pipeline, electrical cable etc.) must remain outside the west to east corridor.	Yes, will be constantly monitored.		Contractor
Foredune conservation	The primary dune system must be designated as a "No-Go" area and no encroachment will be allowed.	Barrier erected to demarcate no-go area. Just needs to be checked regularly.		Contractor
	This area must be actively excluded from the developed area and must not suffer the dumping and other negative impacts that so often accompany building project.	Yes, will be constantly monitored.		Contractor

	The invasive alien vegetation must be removed from the dunes to restore the fragmented areas along the dune. This must be done under the guidance of an Invasive Alien Plant Control Plan.	Yes, been done by appointed botanist. Will be ongoing management thereof.		Contractor/ Botanist
	Beach pathways must be clearly delineated. No movement should be allowed outside of the delineated areas to avoid trampling and to reduce erosion on the foredune.	Yes, pathways done by botanist.		Contractor/ Botanist.
	Gardening and landscaping should not result in removal or destruction of vegetation which will either destabilize a primary or significant dune or cause a significant adverse effect on the dune system due to increased erosion by natural coastal processes or human movement, or detrimentally affect the ecology or habitat.	Yes, will be monitored. Only to start on completion of construction		Contractor

EMPr 61	<b>Heritage (1)</b>			
	Should any heritage remains be exposed during excavations or any other actions on the site, these must immediately be reported to the Provincial Heritage Resources Authority of the Western Cape, Heritage Western Cape. Heritage remains uncovered or disturbed during earthworks must not be further disturbed until the necessary approval has been obtained from Heritage Western Cape. Heritage remains may only be disturbed by a suitably qualified heritage specialist working under a directive from the relevant Heritage Resources Authority. Heritage remains include: meteorites, archaeological and/or paleontological remains (including fossil shells and trace fossils); coins; indigenous and/or colonial ceramics; any articles of value or antiquity; marine shell heaps; stone artefacts and bone remains; structures and other built features with heritage significance; rock art and rock engravings; shipwrecks; and/or graves or unmarked human burials including grave goods and/or associated burial material.	Yes, noted. Will be reported if anything is exposed and discovered. None observed in September 2024		Contractor

EMPr 63	<b>Vegetation Rehabilitation – progressive rehabilitation must be carried out (4)</b>			
	A 100% indigenous planting plan must be adhered to in terms of all planting carried out on the site. Consultation must be made with a Botanical Specialist for a site-specific vegetation list.	Will be done on completion of construction		Contractor/ Botanist
	Erosion prevention and control measures must be implemented. Organic mulch or sandbags must be used to contain all sediment and prevent erosion during rehabilitation.	Will be done on completion of construction		Contractor
	A Landscape consultant be appointed to recommend and implement the introduction of an indigenous landscape plan to protect the existing indigenous vegetation and to prepare a landscape plan for implementation in the private and common areas.	Yes a landscaper has been appointed for common areas.		Contractor/ Botanist

	All disturbed open space areas are to be rehabilitated using locally occurring indigenous vegetation (plant list available in Section 12).	Will be done on completion of construction		Contractor/ Botanist
--	--	--	--	-------------------------

	<b>Best practice (6)</b>			
EMPr p6	In order of priority aim to: avoid, minimise or remedy disturbance of ecosystems and loss of biodiversity;	Constantly being monitored by ECO		EA Holder/ Contractor
	Avoid degradation of the environment and avoid jeopardising ecosystem integrity;	Constantly being monitored by ECO		EA Holder/ Contractor
	Pursue the best practicable environmental option by means of integrated environmental management.	Constantly being monitored by ECO		EA Holder/ Contractor
	Protect the environment as the people's common heritage;	Constantly being monitored by ECO		EA Holder/ Contractor
	Control and minimise environmental damage; and	Constantly being monitored by ECO		EA Holder/ Contractor
	Pay specific attention to management and planning procedures pertaining to sensitive, vulnerable, highly dynamic or stressed ecosystems.	Constantly being monitored by ECO		EA Holder/ Contractor

## Site photographs



1.

Construction signs at entrance of property.



2.

Removed alien vegetation, ready for removal.



3.

Material stored on site. Topsoil stored on site



4.

No-go barriers in place. Building material store on site.



5.

No-go barriers in place.





6.

No oil leaks observed from machine.



 <p>04 Sept 2024 12:59:20 33 Bayview Drive Whale Rock Ridge Plettenberg Bay Garden Route District Municipality Western Cape</p> <p>7.</p>	 <p>04 Sept 2024 12:59:42 33 Bayview Drive Whale Rock Ridge Plettenberg Bay Garden Route District Municipality Western Cape</p> <p>8.</p>	 <p>04 Sept 2024 12:59:54 33 Bayview Drive Whale Rock Ridge Plettenberg Bay Garden Route District Municipality Western Cape</p> <p>9.</p>
<p>Rubble from demolition ready for removed</p>	<p>No oil leaks observed on machinery on site.</p>	<p>No oil leaks observed on machinery on site.</p>
 <p>04 Sept 2024 13:00:38 3957 Aquarius Close Plettenberg Bay Garden Route District Municipality Western Cape</p> <p>10.</p>	 <p>04 Sept 2024 13:01:05 3957 Aquarius Close Plettenberg Bay Garden Route District Municipality Western Cape</p> <p>11.</p>	 <p>04 Sept 2024 13:01:08 3957 Aquarius Close Plettenberg Bay Garden Route District Municipality Western Cape</p> <p>12.</p>
<p>Material stored on site.</p>	<p>Protected tree should be marked properly on all side to ensure no damage occurs.</p>	<p>No-go barriers need to be checked and re-erected regularly please</p>



 <p>04 Sept 2024 13:01:29 3957 Aquarius Close Plettenberg Bay Garden Route District Municipality Western Cape</p> <p>13.</p>	 <p>04 Sept 2024 13:01:54 3957 Aquarius Close Plettenberg Bay Garden Route District Municipality Western Cape</p> <p>14.</p>	 <p>04 Sept 2024 13:03:18 33 Bayview Drive Whale Rock Ridge Plettenberg Bay Garden Route District Municipality Western Cape</p> <p>15.</p>
<p>Toilet on site. Cleaned weekly.</p>	<p>Litter on site.</p>	
 <p>04 Sept 2024 13:04:45 3957 Aquarius Close Plettenberg Bay Garden Route District Municipality Western Cape</p> <p>16.</p>	 <p>04 Sept 2024 14:05:14 Robbeberg Road Whale Rock Ridge Plettenberg Bay Garden Route District Municipality Western Cape</p> <p>17.</p>	 <p>12 Sept 2024 11:49:47 Robbeberg Road Whale Rock Ridge Plettenberg Bay Garden Route District Municipality Western Cape</p> <p>18.</p>
<p>Vehicles parked on site.</p>	<p>Guard house being constructed</p>	<p>All generators to be placed on drip trays in case of oil/fuel spills.</p>



 <p>12 Sept 2024 11:50:13</p> <p>19.</p>	 <p>12 Sept 2024 11:50:33 3957 Aquarius Close Plettenberg Bay Garden Route District Municipality Western Cape</p> <p>20.</p>	 <p>12 Sept 2024 11:50:52 3957 Aquarius Close Plettenberg Bay Garden Route District Municipality Western Cape</p> <p>21.</p>
<p>Waste management not sufficient. Bins with lids and caged bins required on site. Lined caged bin have been placed on site since this pic was taken</p>	<p>Toilets on site.</p>	<p>Building material stored on site.</p>
 <p>12 Sept 2024 11:50:56 3957 Aquarius Close Plettenberg Bay Garden Route District Municipality Western Cape</p> <p>22.</p>	 <p>12 Sept 2024 11:51:09 3957 Aquarius Close Plettenberg Bay Garden Route District Municipality Western Cape</p> <p>23.</p>	 <p>12 Sept 2024 11:52:04 3957 Aquarius Close Plettenberg Bay Garden Route District Municipality Western Cape</p> <p>24.</p>
<p>Litter on site.</p>	<p>Nursery on site.</p>	<p>Dead vegetation to be removed from site as it is a fire hazard</p>





25.

Fencing being erected on the 6m servitude line



26.

No-go barriers.



27.

Fencing being erected on the 6m servitude line



28.

No oil leaks observed on machinery on site.



29.

No oil leaks observed on machinery on site.



30.

Gabions baskets being packed. Guard house being built.



 <p>18 Sept 2024 13:00:36</p> <p>31.</p>	 <p>18 Sept 2024 13:04:08 29 Capricorn Drive Plettenberg Bay Garden Route District Municipality Western Cape</p> <p>32.</p>	 <p>18 Sept 2024 13:05:31 33 Bayview Drive Whale Rock Ridge Plettenberg Bay Garden Route District Municipality Western Cape</p> <p>33.</p>
<p>Protected tree marked to ensure no disturbance.</p>	<p>Fencing being erected on the 6m servitude line</p>	<p>Cement mixed on impermeable areas.</p>
 <p>18 Sept 2024 13:06:10</p> <p>34.</p>	 <p>18 Sept 2024 13:06:14</p> <p>35.</p>	 <p>18 Sept 2024 13:07:56 Robbeberg Road Whale Rock Ridge Plettenberg Bay Garden Route District Municipality Western Cape</p> <p>36.</p>
<p>Pipe installed and manhole constructed. No-go barriers need to be checked and re-erected regularly please.</p>	<p>No-go barriers need to be checked and re-erected regularly please.</p>	<p>No oil leaks observed on machinery on site.</p>



 <p>18 Sept 2024 13:08:04 Robbeberg Road Whale Rock Ridge Plettenberg Bay Garden Route District Municipality Western Cape</p> <p>37.</p>	 <p>18 Sept 2024 13:08:34 Robbeberg Road Whale Rock Ridge Plettenberg Bay Garden Route District Municipality Western Cape</p> <p>38.</p>	 <p>26 Sept 2024 10:07:23 Robbeberg Road Whale Rock Ridge Plettenberg Bay Garden Route District Municipality Western Cape</p> <p>39.</p>
<p>Cement being mixed on impermeable surface.</p>	<p>Guard house being constructed. Small water tank on site for water use.</p>	<p>Section of road filled towards the entrance of the estate.</p>
 <p>26 Sept 2024 10:07:25 Robbeberg Road Whale Rock Ridge Plettenberg Bay Garden Route District Municipality Western Cape</p> <p>40.</p>	 <p>26 Sept 2024 10:08:38 Robbeberg Road Whale Rock Ridge Plettenberg Bay Garden Route District Municipality Western Cape</p> <p>41.</p>	 <p>26 Sept 2024 10:08:43 Robbeberg Road Whale Rock Ridge Plettenberg Bay Garden Route District Municipality Western Cape</p> <p>42.</p>
<p>Water connections, no leaks detected.</p>	<p>Materials stored on site.</p>	<p>Machinery on site. No leaks observed.</p>





43.

Generator not on drip tray. Please ensure drip trays are always in place when generators are used to prevent oil spills.



44.

Gabions being installed.



45.

Water leak observed. Was discussed with contractor. Staff instructed to repair. Thank you.



46.

Access road being prepared by grader.



47.







No-go areas demarcated.



48.

Curbs being installed.

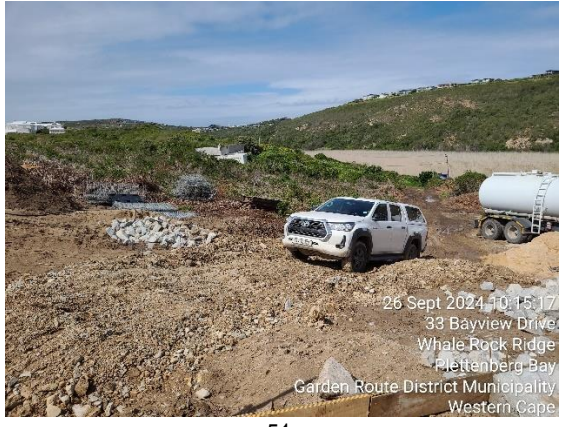

 <p>26 Sept 2024 10:14:34 Robbeberg Road Whale Rock Ridge Plettenberg Bay Garden Route District Municipality Western Cape</p> <p>49.</p>	 <p>26 Sept 2024 10:15:15 33 Bayview Drive Whale Rock Ridge Plettenberg Bay Garden Route District Municipality Western Cape</p> <p>50.</p>	 <p>26 Sept 2024 10:15:17 33 Bayview Drive Whale Rock Ridge Plettenberg Bay Garden Route District Municipality Western Cape</p> <p>51.</p>
<p>No leaks observed on grader.</p>	<p>Stormwater channel next to access road being installed.</p>	<p>Material stored on site.</p>
 <p>26 Sept 2024 10:16:03 Robbeberg Road Whale Rock Ridge Plettenberg Bay Garden Route District Municipality Western Cape</p> <p>52.</p>	 <p>18 Sept 2024 13:06:02</p> <p>53.</p>	 <p>26 Sept 2024 10:13:43 Robbeberg Road Whale Rock Ridge Plettenberg Bay Garden Route District Municipality Western Cape</p> <p>54.</p>
<p>Cement mixed in concrete tray.</p>	<p>Rubble removed.</p>	<p>Caged bin lined with bidum on site for waste. Could not get closer pic as I could not get access to front of property on site visit.</p>



## Conclusion

ECO is overall satisfied that EMPr is being complied with.

Method statement have been received. Thank you

No-go areas demarcated with netting and 6m protected servitude area currently being fenced.

Lined lidded caged bin has been placed on site for waste management.

Machinery on site in good order. No oil leaks observed.

Project Manager must communicate with ECO regarding the next phase and advise when an induction is required for new contractors on site, to ensure all staff complies with authorizations in place.

**90/91 - 99% Compliance**
